

Prestons Park Subdivision

Stages H1 G1 and G2
Geotechnical Completion Report

CDL Land New Zealand Ltd

Reference: 235361

Revision: 0

2023-04-28

aurecon

*Bringing ideas
to life*

Document control record

Document prepared by:

Aurecon New Zealand Limited

Level 2, Iwikau Building
93 Cambridge Terrace
Christchurch 8013
New Zealand

T +64 3 366 0821

F +64 3 379 6955


E christchurch@aurecongroup.com

W aurecongroup.com

A person using Aurecon documents or data accepts the risk of:

- a) Using the documents or data in electronic form without requesting and checking them for accuracy against the original hard copy version.
- b) Using the documents or data for any purpose not agreed to in writing by Aurecon.

Document control							aurecon	
Report title		Stages H1 G1 and G2 Geotechnical Completion Report						
Document code			Project number			235361		
File path		https://aurecongroup.sharepoint.com/sites/235361/5 Deliver Design/Geotechnical/1. Geotechnical Completion Reports/Stage H1 G1 G2/235361 Geotechnical Completion Report Stages H1 G1 G2 Rev0.docx						
Client		CDL Land New Zealand Ltd						
Client contact		Jason Adams		Client reference				
Rev	Date	Revision details/status		Author	Reviewer	Verifier (if required)	Approver	
A	2023-04-05	For review		T. Tremain	J. Muirson		I. McPherson	
0	2023-04-28	Issue to client		T. Tremain	J. Muirson		I. McPherson	
Current revision		0						

Approval			
Author signature		Approver signature	
Name	Tom Tremain	Name	Ian McPherson
Title	Geotechnical Engineer	Title	Technical Director – Ground Engineering

Contents

Executive Summary	4
1 Introduction	6
1.1 Geotechnical Completion	6
1.2 Site Description	6
2 Pre-Development Geotechnical Work	7
2.1 Geotechnical Testing	7
2.2 Ground Conditions	7
2.3 Liquefaction Potential	8
3 Subdivision Earthworks	9
3.1 General	9
3.2 Areas of Cut and Fill	9
3.3 Compaction Quality Control Testing	9
3.4 Compaction Results	9
4 Gravel Embankments	10
4.1 Introduction	10
4.2 Gravel Embankment Details	10
4.3 Gravel Embankment Construction	10
5 Building Development	11
5.1 Technical Category	11
5.2 Earthworks on Building Lots	11
5.3 Soil Suitability Criteria	11
5.4 Building Considerations	11
5.5 Future Earthworks	12
5.6 Construction Observations	12
6 References	13
7 Explanatory Statement	14



Executive Summary

CDL Land New Zealand Limited is developing Stages H1, G1 and G2 of the Prestons Park Subdivision, located on Prestons Road, Christchurch. As part of the work, a geotechnical completion report is required to confirm that the site works have been carried out to the required standard and provide recommendations for building developments. This report describes the earthworks and ground improvement involved with Stages H1, G1 and G2 of the Prestons Park Subdivision.

Based on Aurecon's geotechnical assessment, Stages H1, G1 and G2 comprised six lots classified as Technical Category TC2 and thirty-four lots classified as Technical Category TC1 equivalent prior to earthworks commencing.

Aurecon's role was to monitor the earthworks and fill compaction testing.

Extensive earthworks predominantly comprising filling have occurred on the site. The quality assurance testing of the engineered earth fill indicates that the earth fill placed within the Stages H1, G1 and G2 area has achieved the required compaction levels as per NZS4431:1989 (since superseded by the NZS 4431:2022 '*Engineered fill construction for lightweight structures*').

From the monitoring and testing undertaken as part of the development of Stages H1, G1 and G2 the following is concluded:

Certificate of Compliance

The standard of bulk earthworks generally meets the earthworks specification and the applicable codes, including NZS4431:1989 (since superseded by the NZS 4431:2022 '*Engineered fill construction for lightweight structures*').

Building Considerations

General

This report shall not be used for building consent application for buildings on individual lots. Site specific geotechnical investigations, in-line with NZS3604:2011, shall be undertaken at building consent application stage.

TC1 Foundations

For lots identified as TC1, NZS 3604:2011 type foundations are considered suitable. At the time of writing this report, the location and structural form of the future dwelling on the lots are unknown and this recommendation relates to NZS3604:2011 type lightweight timber or steel framed residential buildings only.

TC2 Foundations

For lots identified as TC2, dwellings shall be founded on TC2 type 'enhanced foundation slabs' as per Options 2, 3 or 4 from the MBIE Guidelines (2012) Section 5.3 to mitigate the effects of liquefaction induced vertical settlement. Alternatively, a specific design in accordance with MBIE Guidelines Section 5.4 could be undertaken by a suitably qualified chartered professional engineer.



Explanatory Statement

This report shall be read as a whole and our explanatory statement is presented in Section 7.

1 Introduction

1.1 Geotechnical Completion

CDL Land New Zealand Limited is developing Stages H1, G1 and G2 of the Prestons Park Subdivision, located on Prestons Road, Christchurch. Stages H1, G1 and G2 are sub-stages within Stage Five of the subdivision. The site works in Stages H1, G1 and G2 included bulk earthworks for the development of the lots. As part of this work, a geotechnical completion report is required to certify the site works have been carried out to the required standard and provide recommendations for building developments.

This report has been prepared for CDL Land New Zealand Limited and issued to Christchurch City Council (CCC). It describes the earthworks involved within Stages H1, G1 and G2 of the Prestons Park Subdivision (see Figure 1 in Appendix A1, A2 & A3 respectively).

The purpose of this geotechnical completion report is to present the following:

- Summarised information from previous investigations carried out as part of the subdivision consent and detailed design;
- Summarised information on the ground conditions and liquefaction risk;
- Extent of earthworks on the lots and compliance testing of bulk earthworks;
- Quality assurance test results for land for the purposes of technical category assessment;
- A summary of the findings, land technical category, and recommendations for building development.

This report has been prepared based on geotechnical data from site observations and compaction testing during and after earthworks construction. All references to cut-fill depths are based on subgrade levels.

This report shall be read as a whole and our explanatory statement is presented in Section 7.

1.2 Site Description

The Prestons Road subdivision is located on the northern fringes of Christchurch City. The site is made up of a series of adjacent properties forming an irregular and elongated rectangle shape, orientated approximately north to south. The total area of the overall Prestons Subdivision site is approximately 190ha. The site can be separated into two distinct blocks. Prestons North runs from the Lower Styx Road in the north through to Prestons Road in the south. Prestons Park continues from Prestons Road, through to Mairehau Road to the south.

The focus of this geotechnical completion report is on Stages H1, G1 & G2 of the Prestons Park Subdivision. Stages H1, G1 & G2 incorporates a block in the southeast part of the Prestons Park Subdivision (see Figure 1 in Appendix A1, A2 & A3 respectively).

2 Pre-Development Geotechnical Work

2.1 Geotechnical Testing

The subdivision consent and detailed geotechnical design for the subdivision included an extensive series of geotechnical investigations. These comprised Cone Penetration Tests (CPT), test pits, groundwater measurements and laboratory testing.

The details of these investigations are presented in the following Aurecon reports:

- *Caldwell Block Subdivision Resource Consent Geotechnical Report*, Revision 0 dated 11 July 2018.
- *Prestons Park Stage Five Gravel Embankment Design*, Revision 0 dated 9 October 2019.

The investigation tests carried out within Stages H1, G1 & G2 of the Prestons Park area are presented in Figure 2 in Appendix A1, A2 & A3 respectively.

2.2 Ground Conditions

From the extensive geotechnical investigations, the ground conditions within the Prestons Park Subdivision were divided into various geological areas. The typical ground conditions in the area are presented in Table 1.

Table 1: Typical ground conditions within Stages H1, G2 and G3.

Depth to Top of Unit (m)	Depth to Base of Unit (m)	Soil Unit
0	0.3 to 0.4	TOPSOIL.
0.3 to 0.4	3	SAND with minor silt, loose to medium dense.
3	12	SAND with minor silt, medium dense to dense.
12	Not determined	SAND, dense to very dense.

Groundwater levels ranged from 1m to 2.5m below ground level. During the site earthworks the above soil profile and groundwater levels were typically encountered within the area of interest.

2.3 Liquefaction Potential

As part of the geotechnical assessment and detailed design, a liquefaction assessment was carried out. The details of the liquefaction assessments are presented in the above reports. The land categorisation was based on the criteria of Ministry of Business, Innovation and Development (MBIE), Technical Category deformation performance limits are set out in Table 2.

Table 2: Technical category definitions and foundation implications (MBIE, 2012).

Technical Category	Liquefaction Deformation Limits				Likely Implications for House Foundations (Subject to individual assessment)
	Vertical		Lateral Spread		
	SLS	ULS	SLS	ULS	
TC1	15mm	25mm	nil	nil	Standard 3604-like foundation with tied slabs
TC2	50mm	100mm	50mm	100mm	MBIE Enhanced Foundation Solutions
TC3	>50mm	>100mm	>50mm	>100mm	Site Specific Measures – Piles or Ground Improvement

The results from the liquefaction assessment, detailed in the geotechnical report dated 11 July 2018, indicated that the Stage Five of Prestons Park Subdivision can be classified as Technical Category 1 (TC1) and Technical Category 2 (TC2).

3 Subdivision Earthworks

3.1 General

Bulk earthworks for Stages H1, G1 and G2 of Prestons were carried out in accordance with the requirements of NZS 4404:2010, “*Code of Practice for Urban Subdivision*” and NZS4431:1989 “*Code of Practice for Earthfill for Residential Development*” (since superseded by the NZS 4431:2022 “*Engineered fill construction for lightweight structures*”). The earthworks typically comprised stripping the site of topsoil, filling using imported pit run gravel or site-won sand, and then replacing topsoil. No excavation to remove in-situ organic material was undertaken as organics were infrequent, typically thin seams if encountered and at depths of greater than 2m.

3.2 Areas of Cut and Fill

Site earthworks within Stages H1, G1 and G2 have included predominantly filling in comparison to the site subgrade levels with some minor cuts. The fill material comprises site-won sand and pit run gravel overlying a natural sand subgrade. A layer of topsoil overlies the fill material. The extent of filling is shown in AB-PS-S5-EW-03 in Appendix A1, A2 & A3 respectively.

3.3 Compaction Quality Control Testing

Independent testing of earthfill compaction completed using conventional earthworks techniques was carried out using a Nuclear Densometer (NDM). The acceptance criterion was based on the Prestons Park Subdivision earthworks specification as follows:

- Compaction of fill is to be in accordance with NZS 4431: 1989 (since superseded by the NZS 4431:2022 ‘*Engineered fill construction for lightweight structures*’).
- Compaction standard is 95% Maximum Dry Density (MDD) for all areas of bulk filling, per NZS4402 Test 4.1.3.

Fill materials comprised of site-won sand and imported pit run gravel. Compaction curves for each of the fill materials are presented in Appendix B.

The MDD from the compaction curves were used to determine the level of compaction required for the fill material. A summary of these NDM results is presented in Appendix C and the NDM testing locations are presented in Figure 4 in Appendix A1, A2 & A3 respectively.

On those occasions where quality control testing did not meet the specification, the Contractor was required to rework the fill to achieve the required compaction.

3.4 Compaction Results

The results presented in Appendix C indicate that 95% MDD or greater compaction has been consistently achieved in the areas of bulk fill. Where NDM results indicated the required compaction had not been achieved, the Contractor completed additional compaction effort and conforming NDM results were achieved. From these results and our site observations, we confirm that the earthfill placed within Stages H1, G1 and G2 have achieved the required compaction.

4 Gravel Embankments

4.1 Introduction

The construction of the pond running to the south of Stage G1 was identified as being a potential cause of lateral spreading in a large seismic event, even with ground improvement by impact rolling undertaken during previous stages. As the liquefiable layers are typically in the upper 2.5m to 3m depth of the soil profile, it was considered more feasible to remove the liquefiable layers and form a compacted gravel embankment to limit the potential hazard.

Lateral spreading requires the need for a continuous liquefiable layer through to the free face. By removing this continuous liquefiable layer and reinstating with compacted gravel, lateral spreading can be limited or eliminated.

4.2 Gravel Embankment Details

The design of the gravel embankments within Stage Five of Prestons Park Subdivision was undertaken by Aurecon and is presented in *“Prestons Park Stage Five Gravel Embankment Design”*, Revision 0 dated 9 October 2019. The gravel embankments were designed to limit lateral spreading displacements to within TC2 acceptable limits, which are given in Table 2. The purpose of the gravel embankments is to intercept the continuous layer of liquefiable soils adjacent to the free edge (basin or open channel), as lateral spreading requires a continuous liquefiable layer.

Depending on the depth and the extent of liquefiable layers near the free face, the gravel embankment size and depth varied. The gravel embankment design comprised compacted AP65 or pit run gravel with a layer of overlying topsoil. The design shape, extent and location of the gravel embankments is shown in PS-S5-EW-05, which is included in Appendix D.

4.3 Gravel Embankment Construction

The gravel embankment design required that a well graded sandy gravel material (such as AP65 or approved pit run) was used for the embankment construction. Material used on site comprised of imported, well graded pit run sandy gravel (AP100). The gravel was topped with approximately 300mm of topsoil. The design drawing required that compaction to 98% of MDD for the gravel was achieved, to ensure that the required embankment design parameters were attained.

Site observations by Aurecon Geotechnical and Civil Engineers confirm the gravel embankments have been constructed with imported well graded pit run gravel. In addition, the compaction quality testing discussed in Section 3 indicates that compaction of at least 95% of MDD has been achieved for the sandy gravel embankment fill material. This level of compaction is slightly less than the 98% of MDD specified in the design drawings but based on our site observations, the gravel embankment will meet the minimum design parameters required to achieve the intended performance of the embankments.

A review of as-built earthworks information provided by the civil engineers indicates that the required toe width and depth of the gravel embankment profile has been achieved. The cut slope angle of the gravel embankment sides was not specified, and the contractor was only required to construct the correct toe width and depth. As-built plans for the gravel embankments are provided in Appendix D.

Based on the intended design and the gravel embankment construction, Aurecon considers that the gravel embankments have been constructed appropriately and lateral spreading exceeding TC2 limits adjacent to the pond is unlikely. From a lateral spreading perspective, the lots adjacent to pond are likely to perform to the level of TC2 equivalent.

5 Building Development

5.1 Technical Category

Geotechnical testing has been carried out as part of the subdivision development. The testing indicates the lots within Stages H1, G1 and G2 are likely to perform to TC1 and TC2 equivalent. The technical category classification of the lots is provided in Figure 5 in Appendix A1, A2 & A3 respectively.

5.2 Earthworks on Building Lots

The extent of earthfill on the lots in Stages H1, G1 and G2 is shown on AB-PS-S5-EW-03 in Appendix A1, A2 & A3 respectively.

The fill areas have been constructed using materials and processes that have been randomly measured by independent testing. The testing shows that the placement of filling is generally in accordance with the specification and relevant standards.

5.3 Soil Suitability Criteria

Section 3 of New Zealand Standard NZS 3604:2011 "*Timber Framed Buildings not requiring specific Engineering Design*" provides several criteria for defining foundation soil suitability for lightweight timber or steel framed residential buildings.

Clauses 3.1.3 and 3.3 of NZS 3604:2011 provide criteria for determining strength and suitability of founding soils. Clauses 3.4.1 and 3.4.2 of NZS 3604:2011 discuss depths to competent founding. For purposes of this report, we have interpreted these clauses as meaning that for sound bearing at depths of 200mm to 600mm, standard shallow type foundations can be used.

For depths greater than this, specific foundation designs could be used or alternatively excavations can be backfilled to the required level with 10MPa site concrete or compacted hardfill. In line with the Client's brief, Aurecon will be undertaking site specific investigations on each residential lot. We will prepare site specific geotechnical reports addressing the foundation requirements on individual building lots. The testing data for the lot specific investigations will be uploaded to the New Zealand Geotechnical Database. For building consent purposes reports prepared for individual lots shall be used.

5.4 Building Considerations

The recommendations in this report shall not be used for individual building consent applications. Site specific investigations in accordance with NZS 3604:2011 are required.

TC1 Foundations

For lots identified as TC1 we consider NZS 3604:2011 type foundations are suitable. We note that at the time of writing this report, the location and structural form of the future dwelling on the lots are unknown and our recommendations relate to NZS3604:2011 type lightweight timber or steel framed residential buildings only.



TC2 Foundations

For lots identified as TC2 we recommend founding dwellings on TC2 type 'enhanced foundation slabs' as per Option 3 or 4 from the MBIE Guidelines (2012) Section 5.1.3 to mitigate the effects of liquefaction induced vertical settlement. Alternatively, in accordance with MBIE Guidelines Section 5.4 a specific design could be undertaken by a suitably qualified chartered professional engineer.

5.5 Future Earthworks

We do not anticipate that future earthworks will be required on the majority of the lots, however should such work be required the following should be noted.

- All earthworks should be carried out in accordance with the Health and Safety at Work Act 2015 and the Worksafe New Zealand Excavation Safety Good Practice Guidelines, 2016.
- Cuts that exceed 0.6m high around any of the house sites must be retained by a suitable retaining wall designed by a Chartered Professional Engineer.
- We recommend that no more than 450mm of fill is placed on the allotment without detailed engineering design.
- Earthworks (cut and fill) should not be undertaken adjacent to any timber retaining wall if present.
- Any development where excavations greater than 1.2m in depth are proposed, must be subject to specific investigation and design to confirm these works will have no adverse effect on land stability, infrastructure and/or structures on adjacent lots. Excavations near sensitive structures or near boundaries may require geotechnical engineering input even if shallower than 1.2m.

5.6 Construction Observations

The suitability of foundation conditions must be verified at the time of construction. Foundation inspections by a Building Inspector or a Chartered Professional Engineer who are familiar with this report must be carried out to ensure the adequacy of the foundation subgrade prior to the placement of granular hardfill or the construction of foundations.

6 References

- Aurecon New Zealand Limited, 2018. *Caldwell Block Subdivision Resource Consent Geotechnical Report*, Rev 0. Christchurch, New Zealand.
- Aurecon New Zealand Limited, 2019. *Prestons Park Stage Five Gravel Embankment Design*, Rev 0. Christchurch, New Zealand.
- Boulanger R.W. and Idriss, I.M., 2014. *CPT and SPT based Liquefaction Triggering Procedures*. Center for Geotechnical Modelling Report No. UCD/CGM-14/01, Department of civil and Environmental Engineering, College of Engineering, University of California at Davis.
- Christchurch City Council, 2010. *Infrastructure Design Standards – Part 4: Geotechnical Requirements*.
- Idriss and Boulanger, 2008. *Soil Liquefaction during Earthquakes*. EERI Monograph Series MNO-12
- Ishihara, 1985. *Stability of natural deposits during earthquakes*. Proceedings, 11th International Conference on Soil Mechanics and Foundation engineering, Vol 1, pp. 321-376.
- Ministry of Business Innovation and Employment (MBIE), 2012. *Repairing and rebuilding houses affected by the Canterbury earthquakes*.
- NZGS, 2005. *Guidelines for the Classification and Field Description of Soils and Rocks in Engineering*. NZ Geotechnical Society Inc, Wellington, New Zealand.
- NZGS/MBIE, 2021. Earthquake geotechnical engineering practice, Module 1: Overview of the guidelines. NZ Geotechnical Society Inc, Wellington, New Zealand, Ministry of Business, Innovation and Employment, Wellington, New Zealand.
- NZS1170.0:2002. *Australia/New Zealand Standard, Structural Design Actions, Part 0: General Principles*. Standards New Zealand, Wellington, New Zealand.
- NZS1170.5:2002. *Australia/New Zealand Standard, Structural Design Actions, Part 5: Earthquake Actions – New Zealand*. Standards New Zealand, Wellington, New Zealand.
- NZS 3604:2011. *Timber Framed Buildings*. Standards New Zealand, Wellington, New Zealand.
- NZS 4404:2010. *Land development and subdivision infrastructure*. Standards New Zealand, Wellington, New Zealand.
- NZS 4431:1989. *Code of practice for earth fill for residential development*. Standards New Zealand, Wellington, New Zealand.
- NZS 4431:2022 *Engineered Fill Construction for Lightweight Structures*. Standards New Zealand, Wellington, New Zealand.
- Robertson and Wride, 1998. *Evaluating cyclic liquefaction potential using the cone penetration test*. Canadian Geotechnical Journal, Vol. 35, pp. 442 – 459.
- Tonkin and Taylor (2013) *Liquefaction Vulnerability Study*, Tonkin and Taylor Report 52020.0200/v1.0. February 2013. 52 pages and 14 appendices.
- Zhang, Robertson, and Brachman, 2002. *Estimating liquefaction-induced ground settlements from CPT for level ground*. Canadian Geotechnical Journal, Vol. 39, pp.1168 – 1180.

7 Explanatory Statement

This report has been prepared for CDL Land New Zealand Limited. It may be made available to others but only in full. As noted above, it shall not be used by any person as a substitute for specific field observations and testing once house sites are confirmed.

This report has been prepared as part of the development of the Prestons Park Stages H1, G1 and G2 Subdivision. It has been prepared to provide the following information:


- To report on the management of the earthworks during construction, including compaction standards of fills.
- To report on the extent of ground improvement and the resulting land technical category.

This report does not remove the responsibility of the Owner / Builder / Building Certifier to satisfy themselves of foundation depth and suitability at the finally selected house location.

Subsurface conditions relevant to construction works should be assessed by experienced Contractors and designers who can make their own interpretation of the factual data provided. They should perform any additional tests as necessary for their own purposes. Subsurface conditions, such as groundwater levels, can change over time. This should be borne in mind, particularly if the report is used after a protracted delay or in wet weather.

It is strongly recommended that any plans and specifications prepared by others and relating to the content of this report, or amendments to the original plans and specifications, are reviewed by Aurecon to verify that the intent of our recommendations is properly reflected in the design. During construction we request the opportunity to review our interpretations if the exposed site conditions are significantly different from those inferred in this report.

This report is not to be reproduced either wholly or in part without our prior written permission.




Appendix A

A1 – G1 Figures

A2 – G2 Figures

A3 – H1 Figures

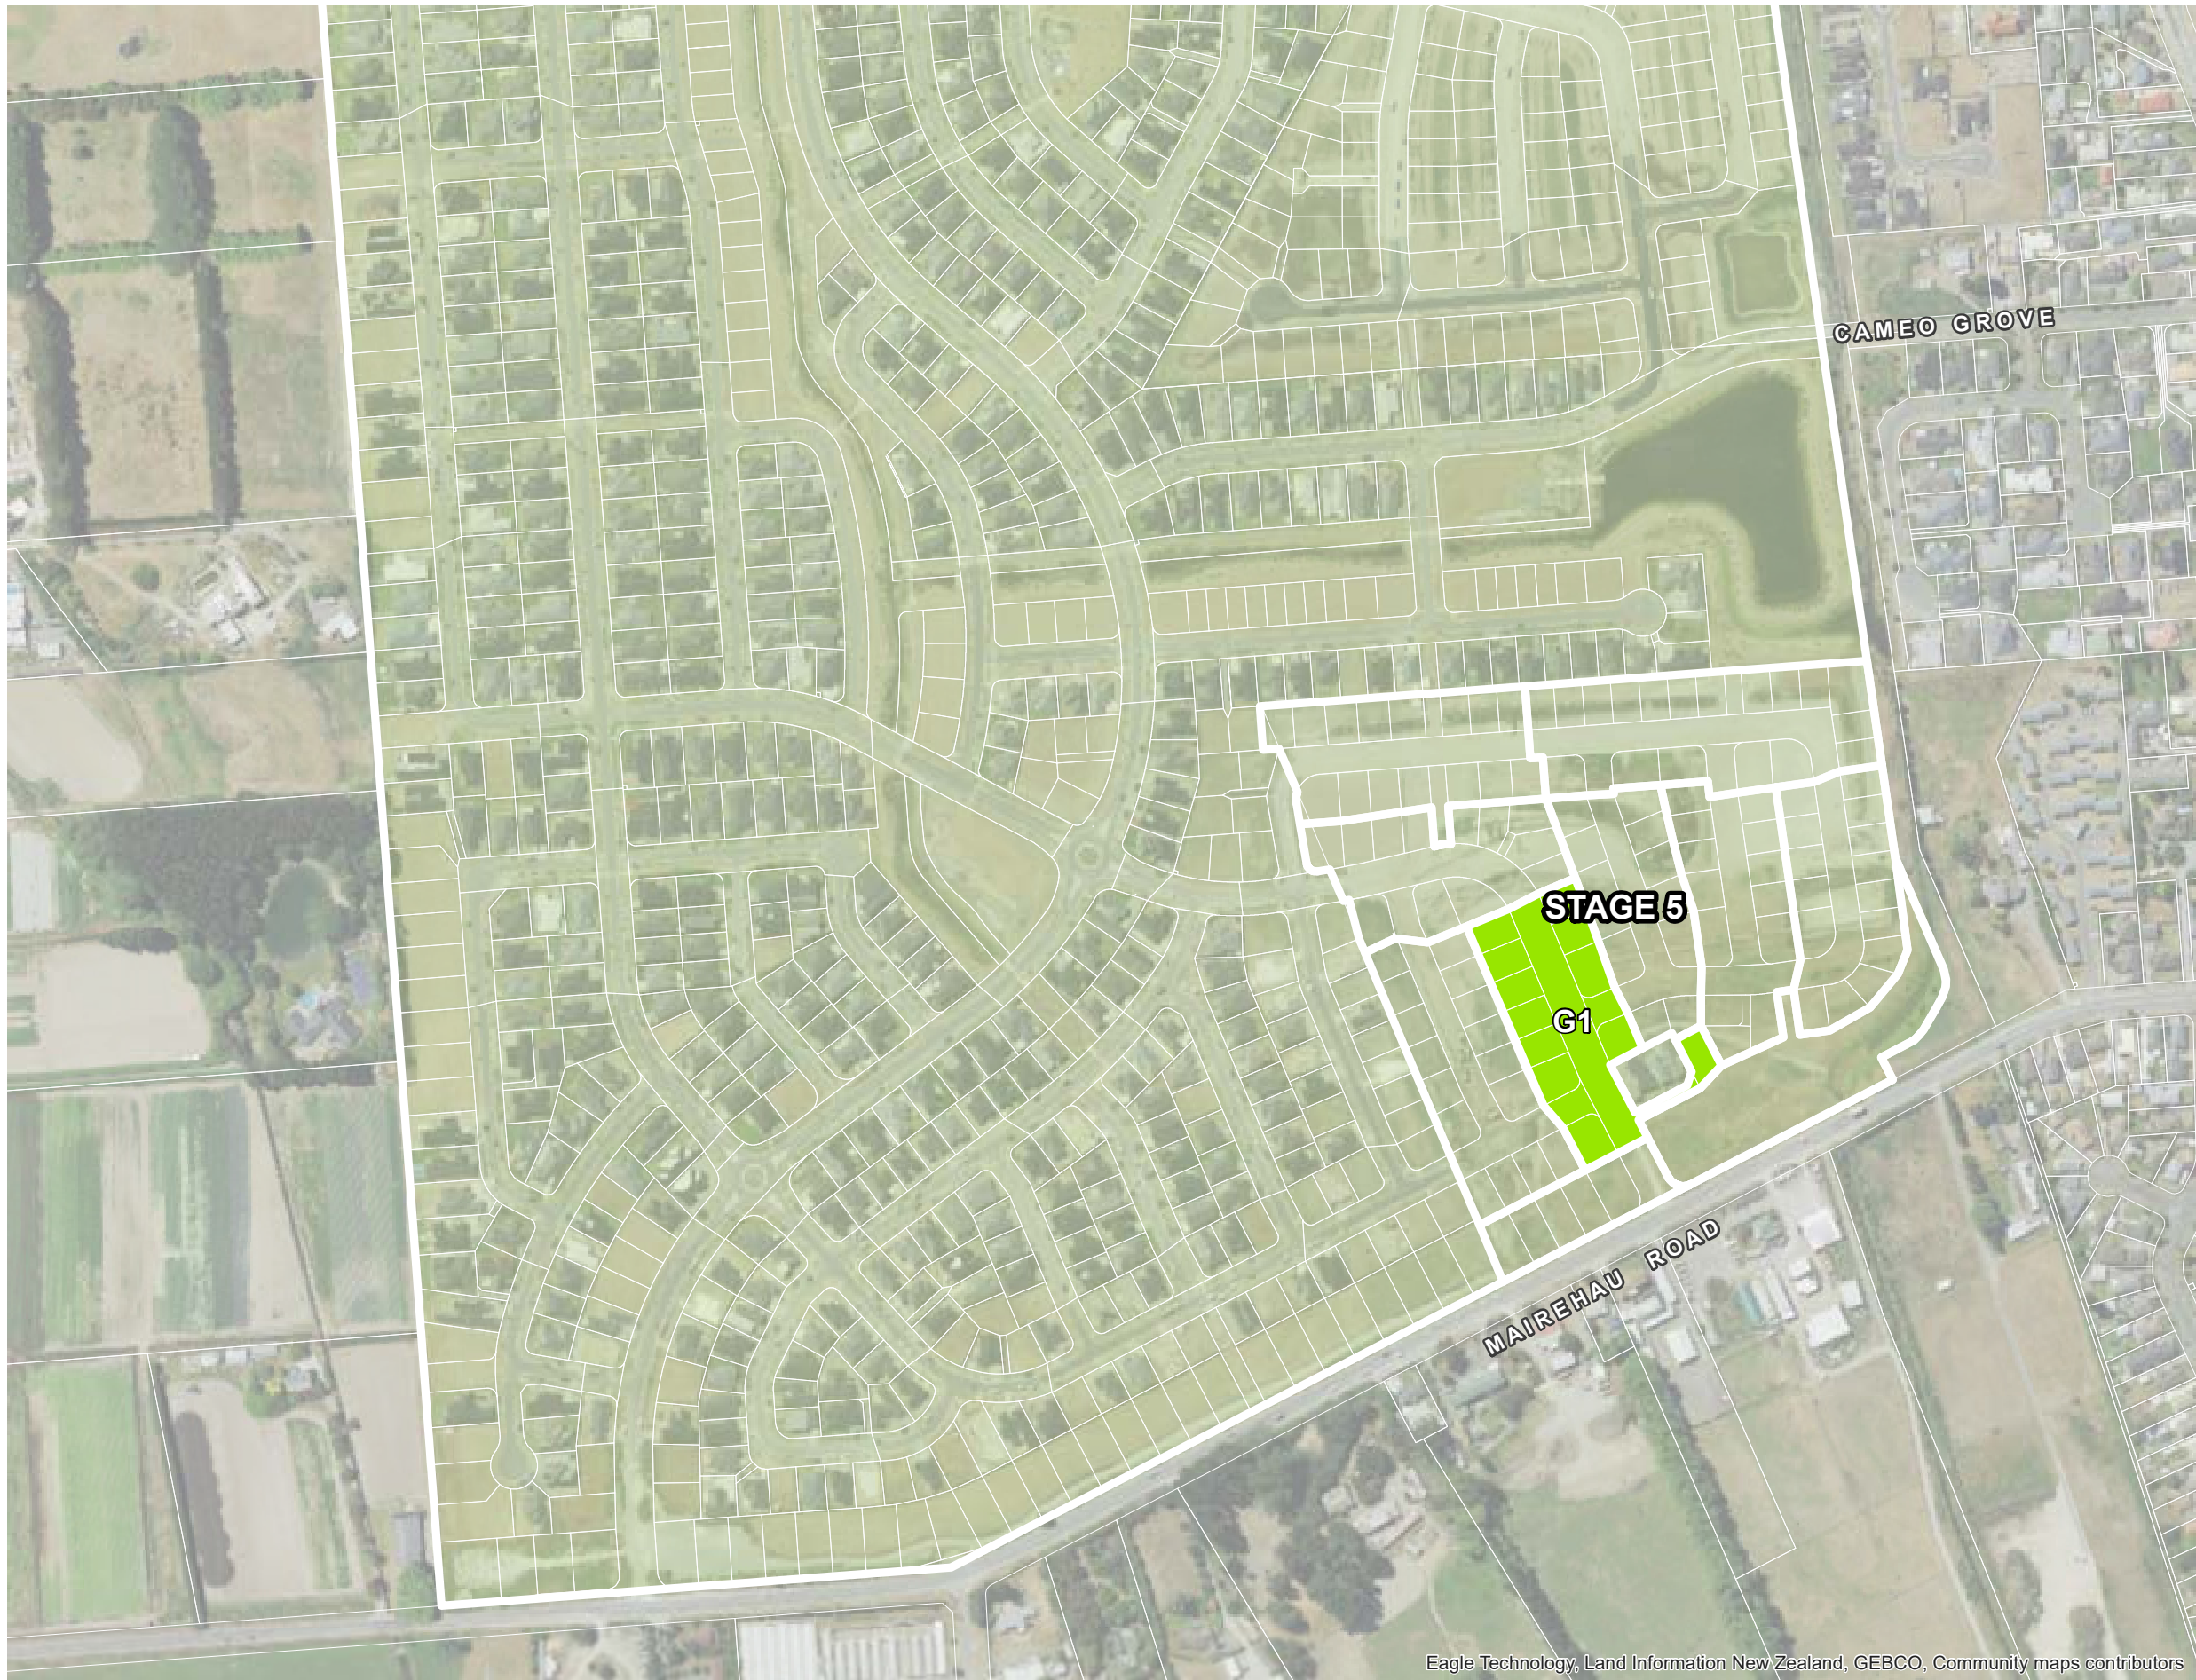

Eagle Technology, Land Information New Zealand, GEBCO, Community maps contributors

NOTES - PROPERTY DATA FROM LINZ
- DEPTH BANDING DATA EXISTING TO FINISHED SURFACE

REV	DATE	REVISION DETAILS	APPROVED
A	23/03/31	ISSUE FOR INFORMATION	J. Kupec

DRAWN	DESIGNED
R.Dawson	T.Tremain
CHIEF	
J. Muirson	
APPROVED	DATE
J. Kupec	31/03/2023

PROJECT
PRESTONS PARK SUB-STAGE G1
TITLE
SITE PLAN

PROJECT No.	235361
SCALE	AS SHOWN
DRAWING No.	FIG 1
SHEET	A

LEGEND

AS BUILT FILL				
Lower_value	Upper_value		Colour	
-3	to	-2.4	m	
-2.4	to	-1.8	m	
-1.8	to	-1.2	m	
-1.2	to	-0.6	m	
-0.6	to	0	m	
0	to	0.01	m	
0.01	to	0.2	m	
0.2	to	0.4	m	
0.4	to	0.6	m	
0.6	to	0.8	m	
0.8	to	1	m	
1	to	1.2	m	
1.2	to	1.4	m	
1.4	to	1.6	m	
1.6	to	1.8	m	



This AS BUILT drawing has been prepared based on
Information provided by the contractor "KB Contracting".

NOTE:

1. FILL BANDING SHOWN IS BETWEEN EXISTING SUBGRADE (STRIPPED EXISTING SURFACE) TO FINISHED SUBGRADE.



CLIENT

REV	DATE	REVISION DETAILS	APPROVED
A	29/03/23	ISSUED FOR INFORMATION	K ASHBY

DRAWN	DESIGNED
A COLUMBUS	A COLUMBUS
CHECKED	
D WATSON	
APPROVED	
K. ASHBY	

PROJECT		PRELIMINARY NOT FOR CONSTRUCTION	
PRESTONS PARK		PROJECT No. 235361	
TITLE		SCALE	SIZE
AS-BUILT EARTHWORKS FILL PLAN SUBSTAGE G1 & G2 STAGE 5		1:500	A1
DRAWING No.		REV	
AB-PS-S5-EW-03		A	

